


SOUTH GIPPSLAND SHIRE COUNCIL

paths & trails strategy 2018



A review and update of the 2010 Paths & Trails Strategy and policy review that includes a prioritised and costed project list with descriptions.

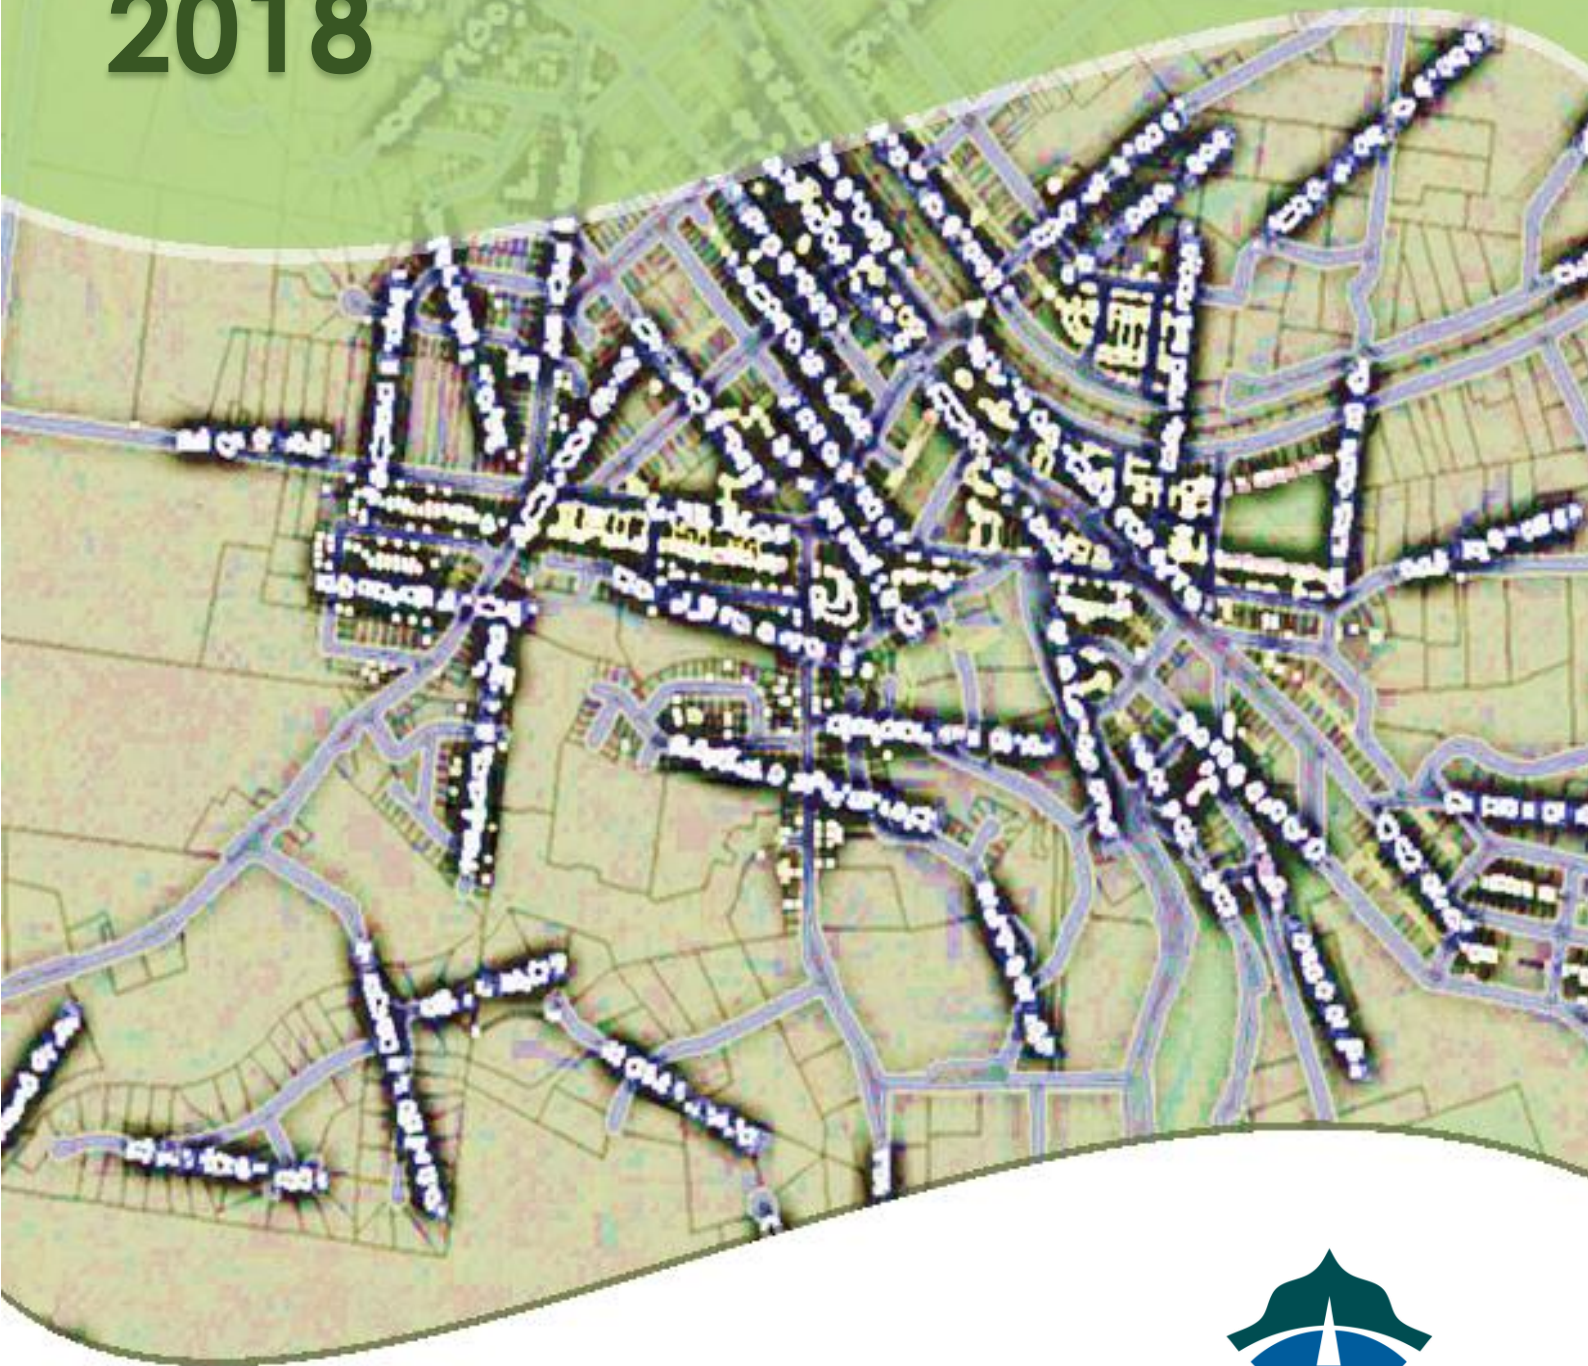

*South Gippsland
Shire Council*



Andrew Nixon Land Use Management

Prepared by:

Andrew Nixon Land Use Management

Postal Address: P.O. Box 528, Mallacoota Vic. 3892

Mobile: 0429 144 270 **Email:** asnix@bigpond.com

DISCLAIMER OF LIABILITY

This report is a document that has been prepared by Andrew Nixon Land Use Management. The consultant has undertaken this analysis in their capacity as advisor in accordance with the scope and subject to the terms associated with this study.

Readers should note that this report may include implicit projections about the future which by their nature are uncertain and cannot be relied upon, as they are dependent on potential events which have not yet occurred. For these reasons and others, facility development is inherently risky and frequently things do not turn out as planned.

In preparing this report, the consultant has relied upon information supplied by third parties: South Gippsland Shire Council, Vic Roads, Bicycle Network, community groups, and individuals, along with publicly available information. The consultant has not attempted to verify the accuracy or completeness of the information provided.

The consultant does not undertake any responsibility arising in any way whatsoever to any person or organisation, except South Gippsland Shire Council in respect of information set out in this report, including any errors or omissions therein-through negligence or otherwise however caused.



*Thanks to the South Gippsland Shire community,
the Staff at the South Gippsland Shire Council,
as well as community groups and individuals
for their contribution to the development of this review.*

contents

1. executive summary	3
2. introduction	5
3. vision	9
3.1 2018 Guiding Principles	9
4. 2010 strategy review	11
4.1 Community Response to the 2010 Strategy	11
4.2 2017 Review Objectives	12
4.3 Significant Changes – Then to Now	12
4.3.1 Design Concerns	14
4.4 2010 Strategy Project Priority List Review	14
4.4.1 Summary of Outcomes	14
4.4.2 Completed Projects	15
4.4.3 SGSC Footpath Extension Program	16
4.4.4 Remaining Projects	16
4.4.5 Funding Outcomes 2010-2017	18
4.5 Funding Opportunities	18
4.5.1 Federal Government	18
4.5.2 State Government	19
4.6 Maps 2010-2017	21
4.7 2010 Project Priority Matrix (PPM)	22
4.8 2018 PPM Revised	25
5. community consultation	26
5.1 Consultation Methodology	26
5.1.1 Inputs into the 2017 Review of the 2010 Strategy	27
5.1.2 Future Community Consultation Methods	28
6. description & assessment of new projects	30
6.1 Great Southern Rail Trail (GSRT)	31
6.1.1 The GSRT: Leongatha to Nyora Extension	31
6.1.2 The GSRT: Welshpool to Hedley Extension	33
6.1.3 Future GSRT Management	33
6.1.4 Consultation / Research	34



6.2	Hoddle Mountain Trail	34
6.2.1	Consultation / Research	35
6.2.2	Hoddle Mountain Trail Route.....	35
6.2.3	Mount Hoddle Trail Issues.....	36
6.2.4	SGSC Resolutions	36
6.3	Waratah Way	37
6.3.1	The Gap to Waratah Bay	38
6.3.2	Consultation / Research	40
6.3.3	Map of Waratah Way.....	41
6.3.4	Outcomes of Community Consultation	42
6.4	Acacia Way, Walkerville	43
6.4.1	Consultation / Research	44
6.5	Walkerville Foreshore Shared Path.....	45
6.6	Mossvale Park	45
6.6.1	Consultation / Research	46
6.7	Agnes River Road Walk.....	46
6.7.1	Consultation / Research	47
6.8	Mountain Bikes.....	48
6.9	Coal Creek to Ritchies Reserve	49
6.10	Isabella Blvd to Hannah Rise Crescent Shared Path	49
7.	2018 strategy review	50
8.	2018 action plan	51
8.1	2018 Strategy Action Plan.....	52
9.	appendices	56
9.1	2018 Project List	57
9.1.1	Construction Projects	57
9.1.2	Linemarking and Signage Projects	59
9.1.3	Projects on VicRoads Roads	60
9.2	Costs Table	61
9.3	Gale Street Preliminary Costs for “Waratah Way”	63
9.4	References	65
9.4.1	Design Standards	65
9.4.2	Strategic Documents	65

1. executive summary



The vision of a rail trail that bisects the South Gippsland Shire creating a central active transport spine is within reach after twenty years of the initial section of the Great Southern Rail Trail (GSRT) being constructed.

The central rail trail 'spine' provides the opportunity from which other connecting paths and trails can eventually radiate, linking South Gippsland's towns and communities.

The 2018 Project List (**Appendix 1**) continues to reflect this strategy, the focus still on establishing the 'spine'. The list proposes a variety of 'spurs' in the form of shared paths, on-road cycle lanes, walking trails, and combinations of all these. The aim is to provide viable, safe, interesting connections, and networks between towns, points of interest, and other destinations. These proposed networks and links will, as a result, offer the community health, social, environmental, and economic benefits far into the future.

A common matter raised with several new projects is the retrofitting of a desired standard of infrastructure into limited space combined with unresolved land tenure



issues. For these to succeed, the process requires good planning, negotiating, and a lot of good will.

Of the ninety six (96) projects listed in the 2010 Strategy:


- Seventeen were completed; **18%**
- Ten are in the 'pipeline', i.e. either nearly completed, designed, budgeted, or a part of another project. For example, the Foster, Loch, and Korumburra streetscapes; **10%**
- Two were partially completed and there are no further plans to extend; **2%**
- One will not be completed (Toora to Tin Mine Road); **1%**
- Leaving sixty-six projects; **69%** from 2010 unresolved as:
 - Many are cycle lanes that create circuits in towns. These don't receive high ratings usually because they are a single user type and although safer, they are still not ideal.
 - The major inter-town cycle routes are primarily on VicRoads managed roads which doesn't have the funding to provide the works necessary.
 - Some just didn't meet the assessment criteria well enough (and therefore have a low priority).
 - Some of which could be regarded as 'nice to do' and might be constructed in an ideal world with unlimited funding.

The Footpath Extension Program has been successful outside of the of 2010 Strategy and has been separated from the 2018 Project List and will continue to operate with a separate budget.

Communities consistently consider paths and trails as high priority projects when asked by Council during the community planning processes. This feedback helps confirm survey data that walking, cycling, and horse riding constitute the largest recreational activity group undertaken by community members. This assumption is corroborated by all recreation research carried out in the past twenty years¹.

¹ Exercise, Recreation and Sport Survey (ERASS) was a joint initiative of the Australian Sports Commission and State and Territory Departments of Sport and Recreation, conducted on an annual basis between 2001 and 2010. ABS Participation in Sport and Physical Recreation data for 2013-14


2. introduction

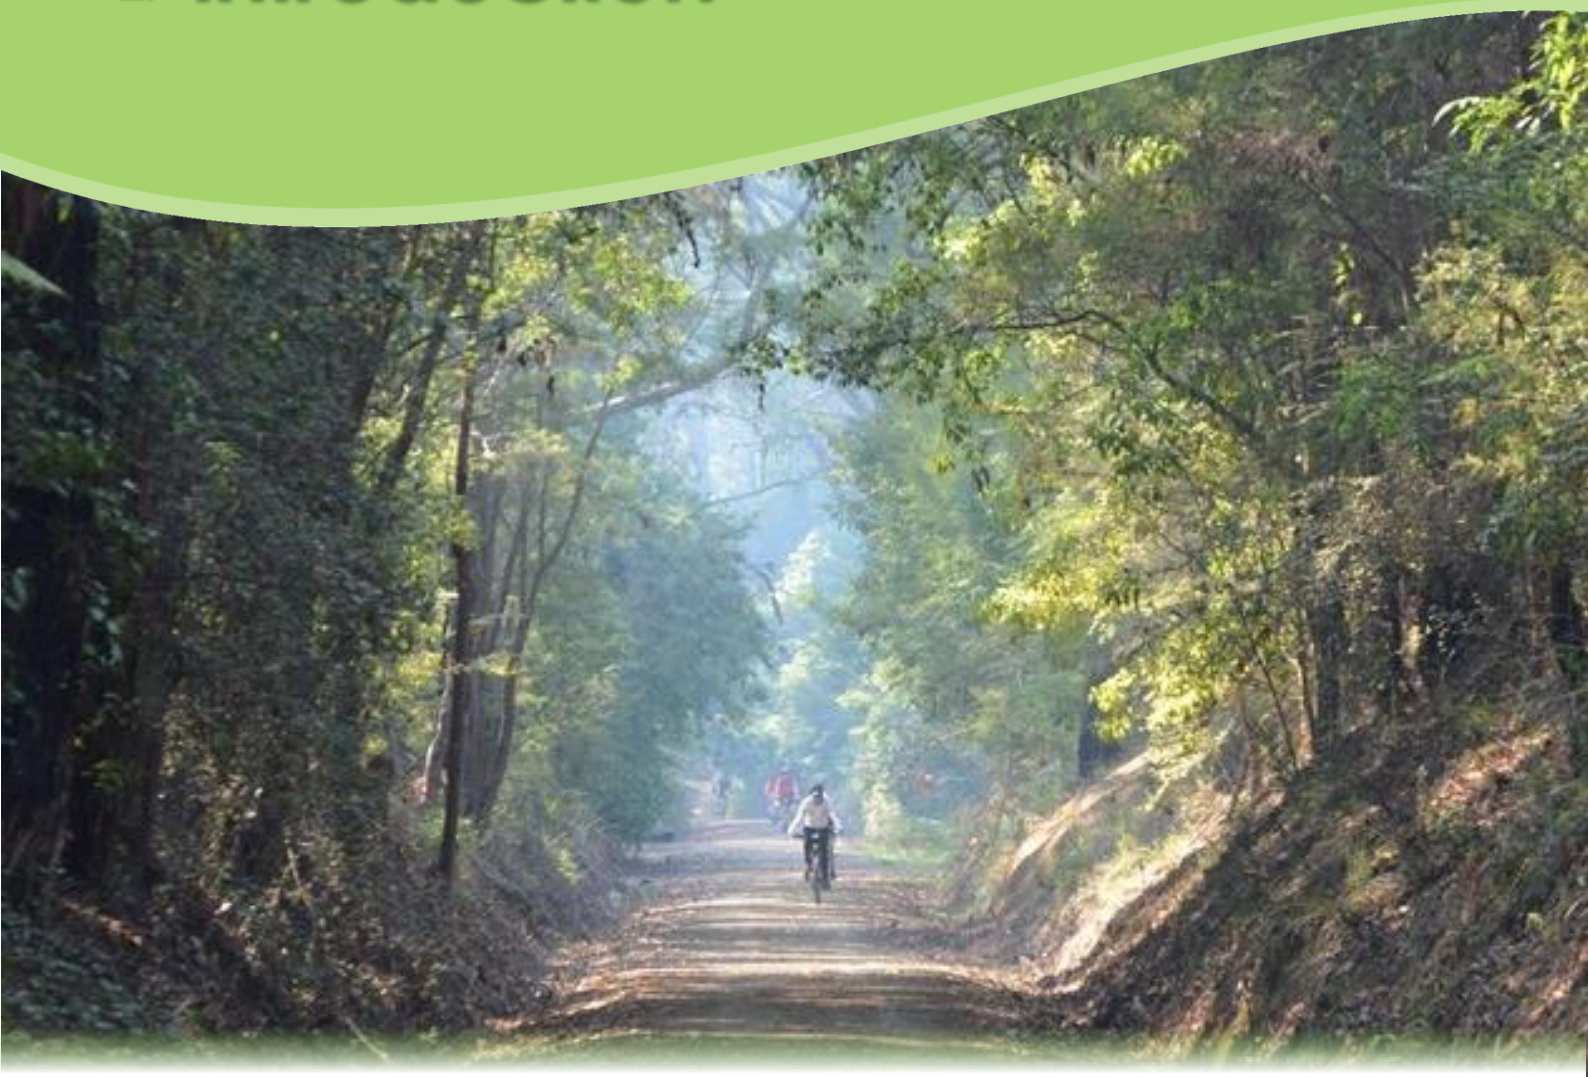

The 2010 Paths & Trails Strategy (2010 Strategy) is a result of recommendations in the South Gippsland Shire Council (SGSC) Recreation Plan 2007 and its sister document, the SGSC Open Space Strategy 2007, to update and review the 2001 Bicycle/Walking/Riding Paths & Trails Strategy (2001 Strategy).

With the successful completion of several sections of the GSRT, the unfortunate demise of the tourist rail, and suggestion of several other shared paths by the South Gippsland community, Council identified the need to desktop review / update of the 2010 Strategy and incorporated it in its Council Plan 2017-2021.

The flowchart below illustrates the basis of the current 2010 Strategy review.

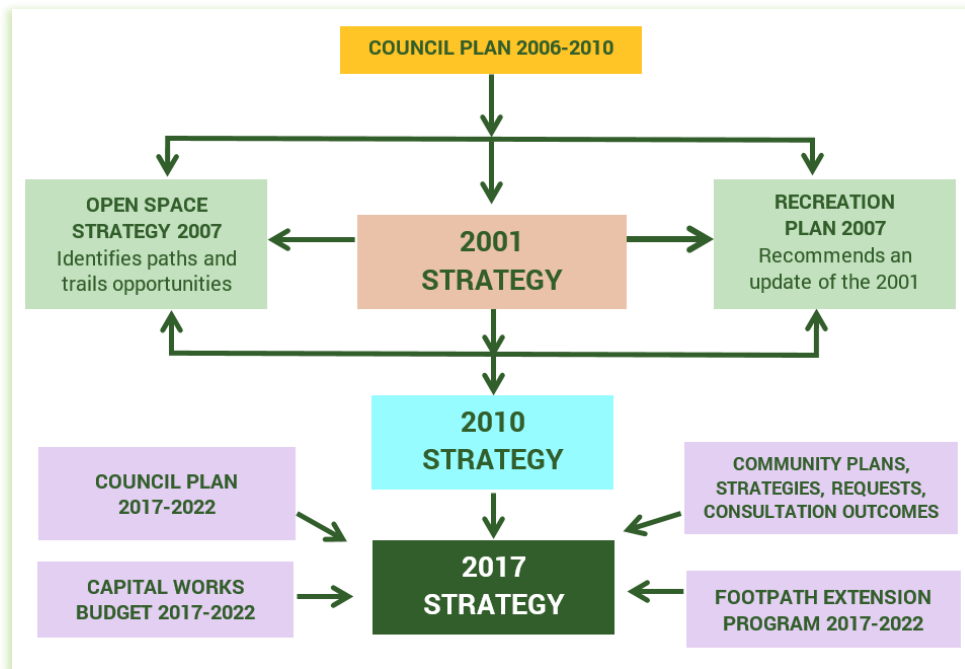

Flowchart of 2010 Paths & Trails Strategy Review

SGSCs 2017 review of the 2010 Strategy looks at how effective the strategy was in application over the past seven years. The Project Priority Matrix (PPM) aims to provide an improved decision-making process whereby future paths and trails can be assessed against each other using value parameters and weightings. These investment decisions will often be made in conjunction with grant funding opportunities.

The 2017 review is a result of a desktop consideration of the many community studies and plans derived from Council’s consultation with the community which seeks to determine and identify the community’s needs and aspirations. A search of the SGSC internal documentation relating to paths and trails included requests, letters, and submissions. Paths and trails feature heavily in many of these community documents. Residents of the Shire have a strong interest in participating in walking (running), cycling (including club competition) and horse riding as recreational activities and in fact underpins the sometimes-overlooked

fact that walking, together with cycling, constitutes by far the largest recreational activity/activities in Australia².

This review reconfirms previous projects and provides a brief synopsis of some new projects. The types of projects on the 2018 Project List (*Appendix 1*) include:

- Off-road shared paths;
- Off-road walking paths;
- Sealing road shoulders and line marking for safer cycling; and
- Improving bicycle signage of designated routes.

The linking of gaps in the footpath network to ensure connectivity to destinations in urban areas is managed through the Footpath Extension Program which is now separated from this strategy.

The associated 2018 Project Priority Matrix (PPM) defined on page 25 seeks to provide a method of determining the priority of projects using a weighting system based on a range of both qualitative and quantitative values (these are open to discussion as there is little empirical data and therefore the allocated values are subjective). It is anticipated that PPM will be used as an ongoing assessment tool that is modifiable, updatable, and is responsive to changing community needs, available funding, and accessible to both the Council and the community as a reference document. A summary of the projects and priorities is included in *Appendix 1*.

To improve the relevance of the PPM in the decision-making process, consideration could be given to the use of recognised data collection and analysis methods to collect asset user and economic data to help support or clarify project priority assumptions. This data will in turn assist in Council's decision-making process. Some data collection methods include counting (infra-red) equipment, cameras, student driven surveys of users, video survey methods, economic modelling, and surveys of business can all help focus future paths and trails planning and assist in assessing the outcomes of the past decisions associated with the Paths & Trails Strategy. Some of these methods are currently being considered by staff.

² Participation in Sport and Active Recreation, Australia 2011-12 Report



The Shire has a slow growing population³ at an annual growth rate of 1.4% (Shire average)⁴ with a high proportion of older persons. The ageing population can be attributed to the Shire being seen as a highly desirable retirement destination and younger people moving away for work, education and other opportunities.

This review, as did the 2010 document, considers equestrian trails. A separate network for this user group has not been developed. Horse riders are generally restricted to dedicated private trails, bush trails in State parks, quiet country roads and rail trails. Examples are the GSRT, several proposed paths described in the Nyora paths feasibility study and the Welshpool – Port Welshpool shared path. Future options may include the proposed Leongatha to Nyora section of the GSRT, Nyora to Cranbourne, and the Nyora to Anderson rail trails.

³ Based on available data (ABS & id – The Population Experts website)

⁴ SGSC Blueprint For Social Community Infrastructure 2014- 2029

3. vision

The overarching vision for the 2018 Paths & Trails Strategy is:

To develop South Gippsland's walking, cycling, and horse riding pathway network for all abilities, and where practicable, safely connect South Gippsland's residents, businesses, and visitors to town centres, schools and main tourist attractions.

The 2018 Strategy implementation actions can be found in ***Section 8 – 2018 Action Plan.***



3.1 2018 Guiding Principles

To achieve this vision, seven principles are listed which provide a guiding framework for the development and implementation of a successful walking, horse riding, and cycling network as follows:

① THE SOUTH GIPPSLAND EXPERIENCE

Capitalise on South Gippsland's spectacular surrounds, providing a range of memorable and unique journeys through its diverse landscapes. Regional trails will traverse and connect to the coast, plains, and wetlands in the south, farmland and rolling hills around the GSRT, natural bushland and hills in the north.

② HEALTH & WELLBEING

Enhance the health and wellbeing of the community by providing the safe environment and infrastructure that supports participation in local recreational experiences. Being active supports good physical and mental health. The walking, horse riding, and cycling network will create walkable neighbourhoods, enjoyable recreational experiences, as well as an increased sense of social connectedness within the local community.

③ ALL ABILITIES ACCESS

The walking, horse riding, and cycling network will be inclusive of people with mobility difficulties including people in wheelchairs, prams, and mobility scooters. Infrastructure such as Disability Discrimination Act (DDA) compliant paths, ramps, and rest areas will be prioritised on appropriate trails.

④ SAFETY & PERCEPTION

Create a safe and comfortable walking, horse riding, and cycling environment for all users. Priority will be provided to pedestrians, horse riding, and cyclists, over motor vehicles along key routes and within town centres. People will feel safer using the streets and trails that have increased passive surveillance and improved lighting.

⑤ CONNECTING PEOPLE & PLACES

An integrated and more accessible network will provide convenient access for locals and visitors to town centres and key destinations. Strategic links and pedestrian priority routes will support walking, horse riding, and cycling as the preferred transport option when moving through town centres, to and from schools, and making local trips. Importantly, the network will strengthen the existing stop and drop zones in South Gippsland. Additionally, the regional trail network will connect townships across the Shire and beyond.

⑥ AWARENESS & EDUCATION

Create an environment in South Gippsland Shire where walking, horse riding, and cycling are logical and enjoyable travel options. Break down the social and psychological barriers that prevent walking, horse riding, and cycling by raising awareness of the many benefits of being active. Support community events, education programs, as well as a comprehensive signage and wayfinding strategy to promote local opportunities.

⑦ ECONOMY AND TOURISM

High quality infrastructure contributes to a healthy and strong local economy and adds to the visitor experience, enhancing the prosperity of the community. Council will work with stakeholders to increase economic growth and employment prospects. It will develop policies and pursue projects to improve the capacity of local residents and business to be part of this growth.

4. 2010 strategy review



4.1 Community Response to the 2010 Strategy

The 2010 Strategy provided a detailed approach to assessing community projects. The community understood that rankings didn't preclude any project if circumstances arose that allowed individual projects to proceed, such as specific funding opportunities. As an example, the community recognised the potential of the GSRT to the Shire with its potential flow-on effects.

Nevertheless, the Shire also got on with implementing some local projects of lower priority. Many projects put forward through the 2010 consultation process would have been great to get up but are beyond the current resources available in the suggested time frames. An example are the difficulties identified in the shared path linking the GSRT in Foster to Wilsons Promontory. Perhaps once the full GRST has been constructed and more Council funding and resources become available, efforts can be directed to developing some of these major spur links.

4.2 2017 Review Objectives

This 2017 review is to:

- Review the 2010 Paths & Trails Strategy and examine how effective it was, i.e. what were the outcomes and how it can be improved.
- Determine what the community and user expectations are and what can realistically be achieved where stated.
- Establish a hierarchy of the most appropriate routes, trails, paths, linkages, and circuits, and developing a list of priority projects by three (3) Project Classes; Construction Projects, On-road Linemarking & Signage Projects, and Projects on VicRoads Roads (*Appendix 1*).
- Update and establish the cost of constructing bicycle, walking, riding paths, and trails, and to review and examine alternative methods and materials using the rates (*Appendix 2*).
- Determine ongoing management responsibilities, particularly maintenance being the highest cost, together with risk and liability. Provide a strategic approach to the provision of a comprehensive cycling and walking network.
- Present review outcomes for Council including a draft five plus year action plan (*Section 8*).
- Provide some recommendations for improved processes relating to SGSCs paths and trails.

4.3 Significant Changes – Then to Now

Much of the information contained in the 2010 Strategy is still current and holds true for today. There has been some updating of design specifications and design philosophy by Austroads / ARRB (and other bodies). These changes include specifications on shared path width, methods to achieve separation of users, on-road cycle lane design, curve radii limits, and construction materials (rolling surfaces). The relevant information on design standards can be found at:

<https://www.onlinepublications.austroads.com.au>.

Incident data and user surveys, primarily from urban (city) shared pathways, indicates that separation of users (walkers, cyclists, horse riders, and cars) is of

critical importance. The conflict occurs due to the differing speeds, vehicle size, use patterns, and space available, for example:

- Cyclists can travel much faster than walkers.
- Walkers (recreational) tend to wander especially those with dogs.
- Horses due to their size can intimidate and block other users.
- Pedestrians, cyclists, and horse riders, although legally able to use any road, do not mix well, particularly in numbers for the above reasons.

The changes to design/construction standards reflect these issues by recommending:

- The widening of paths (2.5 metres or more, 4 metres would be nice!) and/or recommending complete separation of users by constructing separate paths.
- By providing a physical barrier (e.g. 'w' section traffic barriers) for which the style would depend on the road's speed limit.
- Improving surface materials, with the aim of improving rolling speed, stability, and life span/maintenance costs.
- Differentiating the surface colour (buff coloured stone in a spray seal etc.) providing a visual cue for drivers.
- Guide posts as a visual barrier, cue for motorists.
- Separate user paths.

These items can significantly increase the construction costs for any proposal and usually result in a multitude of design and construction options that need to be considered early on in the community consultation and development process.

For example, placing users on a formal or recognised 'shared path' on a road shoulder that adjoins a 100kph road with no vehicle - pedestrian separation is a high-risk strategy that doesn't meet Council's *'duty of care'*. Cyclists and pedestrians can and do currently use road shoulders on rural roads as the only realistic option. The difference is the formality of the route.

Engineering solutions used to resolve such safety issues include:

- Reducing the speed limit;

- Pushing the path further into the road reserve to achieve greater separation from vehicles;
- Highlighting the path by colouring the surface; and
- Constructing barriers.

4.3.1 Design Concerns

Shared cycle and parking lanes are now viewed as virtually unworkable as a single parked car pushes the cyclists onto the traffic lane creating an unacceptable risk. Cycle lanes adjacent to parking lanes without separation have caused many incidents, i.e. drivers opening car doors in the path of cyclists being the major issue. As a result, authorities are reluctant to implement this style of cycle route.

4.4 2010 Strategy Project Priority List Review


4.4.1 Summary of Outcomes

The Project Priority List from the 2010 Strategy has been reviewed to determine the status of the ninety-six (96) projects listed as of 2017 (***Note:** The 2010 Project Priority List included footpath proposals from the 2010 Footpath Extension Program).

Of the ninety six (96) projects listed in the 2010 Strategy:

- Seventeen were completed; **18%**
- Ten are in the 'pipeline', i.e. either nearly completed, designed, budgeted, or a part of another project. For example, the Foster, Loch, and Korumburra streetscapes; **10%**
- Two were partially completed and there are no further plans to extend; **2%**
- One will not be completed (Toora to Tin Mine Road); **1%**
- Leaving sixty-six projects; **69%** from 2010 unresolved as:
 - Many are cycle lanes that create circuits in towns. These don't receive high ratings usually because they are a single user type and although safer, they are still not ideal.
 - The major inter-town cycle routes are primarily on VicRoads managed roads which doesn't have the funding to provide the works necessary.

- Some just didn't meet the assessment criteria well enough (and therefore have a low priority).
- Some of which could be regarded as 'nice to do' and might be constructed in an ideal world with unlimited funding.

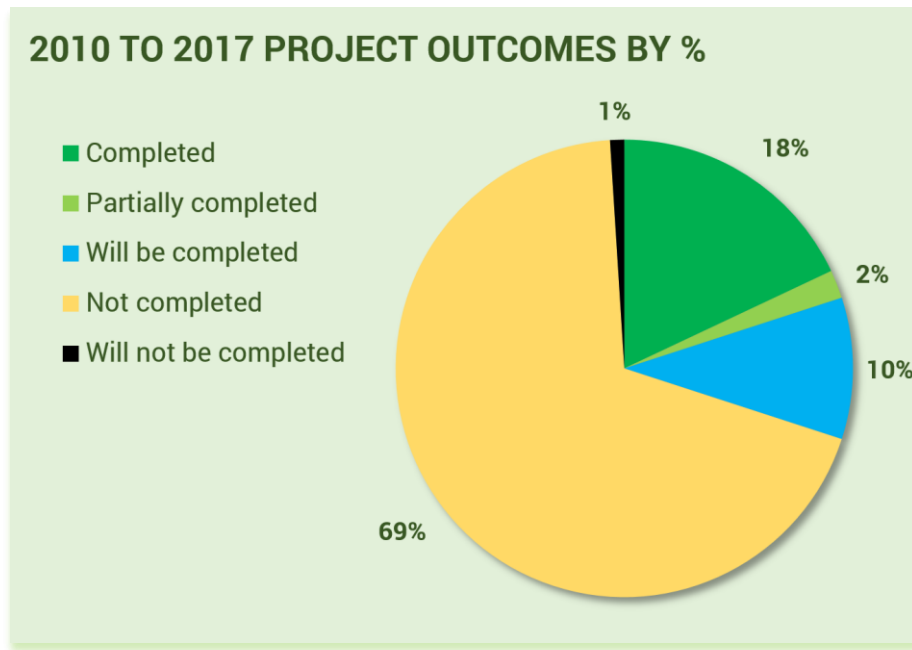

Status Snapshot of the 2010 Strategy Projects

4.4.2 Completed Projects

Several large projects were completed in the past seven years including four sections of the GSRT:

- Foster to Toora.
- Toora to Welshpool.
- Upgrade of the Welshpool to Port Welshpool Trail – completed with savings from the Toora to Welshpool GSRT funding.
- Koonwarra to Meeniyar Black Spur section which included substantial bridge remediation / replacement.

These projects received substantial funding from the Victorian State Government and the SGSC.

Several shorter off-road shared paths were completed:

- Toora to the Toora Recreation Reserve: by the SGSC.

- The extension of the Tarwin Lower/Venus Bay shared path along Jupiter Boulevard to the Venus Bay shops: by the SGSC.
- The Roy Henderson Trail, Manuka Street to Shallow Inlet: by the Sandy Point Foreshore Committee of Management (CoM) and Department of Environment, Land, Water and Planning (DELWP).
- Strzelecki Highway – north side, from Wanke Road to Balook Street: by the SGSC.
- Port Welshpool – along Corner Inlet from Long Jetty Caravan Park to the public toilets: by the SGSC.

4.4.3 SGSC Footpath Extension Program

Many of the projects listed in the 2010 Strategy were urban footpaths. The Footpath Extension Program (FEP) was included in the 2010 PPM. Most of those items included from the FEP focused on connecting disparate sections of the existing urban footpath network. Due to FEPs standalone budget and for the sake of streamlining this review document, the FEP has been removed from the 2018 Project List and is managed separately.

The Forward Capital Works Program budget identifies continued funding for the FEP at varying levels reflecting the community support for this program.

4.4.4 Remaining Projects

The project list in 2010 was intentionally an extensive 'wish list'. All projects that fell under the broad heading "Paths and Trails" that had been identified by the SGSC, the community, and external authorities, were included to show what was being considered by the broader community and could, as a result, be considered against each other. Many were not feasible due to topography, land ownership, area constraints, and some were / are just too costly.

The community repeatedly identifies the need for safe cycling, horse riding, and walking i.e. not on roads mixing with vehicles. Unfortunately, in the attempt to create logical and effective links between facilities and destinations, some on-road routes are unavoidable. By creating a cycle lane or directing users onto the road implies a 'duty of care' upon the SGSC. This duty of care can be achieved through good design using recognised standards. However, in many cases, retrofitting a

lane or path onto existing infrastructure will not allow Council to meet those standards without expensive engineering solutions and/or land purchases/lease etc.

When designing a path/trail/lane, safety is of the highest consideration. Recognised standards are followed to ensure all safety issues are addressed and the SGSC does not expose itself to unnecessary liability risks.

The above scenario partly explains why some paths, cycle lanes, and cycle line marking haven't been completed. For example, the shared path from the Korumburra Secondary College to Radovick Street Korumburra requires a width that is not available along the road reserve and may require some land acquisition. It is still highly rated in this document and may need stronger community support to drive it. Sections of the cycle network which includes Jumbunna Road is listed on VicRoads '*Principal Bicycle Network & Strategic Cycling Corridors Gippsland*' as a priority and as such may be suitable for funding from VicRoads.

Most streets and roads in South Gippsland fall below the critical traffic volume of 3,000 vehicles per day and hence don't trigger the Austroads, AARB design, and Australian Standards (AS) criteria. This combined with low request numbers by the community (2017 request review) to Council has resulted in no new cycle lane marking carried out in the intervening years.

One site that achieved a fairly high priority ranking and recommended as a trial site in the 2010 Strategy was the intersection of Ogilvy Street (Nerrena Road) and the South Gippsland Highway. Since then, the Leongatha heavy vehicle alternate route has been completed resulting in a redesigned intersection with traffic lights and pedestrian crossing points across the South Gippsland Highway and a bike holding / stopping space at the intersection. However, there are no marked designated lanes coloured or otherwise linking cyclists over the rail bridge (no space) to the west or linking back to the lanes marked in Ogilvy Street. This situation could easily be rectified and is listed in the 2018 Project List (projects on VicRoads roads).

Most of the 2010 on-road cycle lane / network recommendations still stand and have been included in **Appendix 1** as part of this review for ongoing consideration by the community and the SGSC as populations and cycle use steadily increase.

4.4.5 Funding Outcomes 2010-2017

Significant funding from the Federal Government, Victorian Government, and the SGSC was secured by Council for the completion of the Foster to Welshpool / Port Welshpool and Black Spur sections. Now completed, the rail trail runs uninterrupted from Leongatha to Welshpool, a length of seventy-two kilometres.

The remaining projects were funded by the SGSC from the Capital Works Program budget. DELWP and Parks Victoria contributed to the construction by the Sandy Point Foreshore Committee of Management of the Ray Henderson path.

Some community driven paths and trails projects were partially funded by the SGSC Community Grants Program.

Many Federal Government funding programs have, over the past seven years, been reduced or discontinued. Examples of discontinued programs are the:

- Provincial Pathways Program
- Small Towns Development Fund
- Regional Partnerships Program

Funding through the State Government programs were reasonably successful with money coming from the Premier's Community Support Funding.

Sometimes funding has been opportunistic. The 2010 Strategy provided strategic and planning support for funding programs when new grants became available.

4.5 Funding Opportunities

There are several Federal, State, and Local Government grant programs. These mainly focus on improving infrastructure for safety and connectivity.

4.5.1 Federal Government

Building Better Regions Fund

The Building Better Regions Fund will invest nearly \$500 million over four years in infrastructure projects and community investments to create jobs, drive economic growth, and build stronger regional communities into the future.

Community Development Grants Program

The Australian Government has established the Community Development Grants Program to support needed infrastructure that promotes stable, secure, and viable local and regional economies.

National Stronger Regions Fund

The National Stronger Regions Fund invests in infrastructure projects which deliver economic benefit and address disadvantage.

Stronger Communities Program

The Stronger Communities Program is providing \$67.5 million over three funding rounds that commenced in 2015/16.

Regional Growth Fund

The Australian Government will provide \$472.2 million over four years from 2017/18 to establish the Regional Growth Fund.

4.5.2 State Government

Several of the programs below are linked to the Federal funding initiatives but are administered and enhanced by the Victorian State Government.

Regional Jobs and Infrastructure Fund

The Regional Jobs and Infrastructure Fund (RJIF) is the Victorian Government's overarching regional development package. It invests in growing jobs, building infrastructure, and strengthening communities in regional Victoria.

Regional Development Victoria (RDV) manages the RJIFs three programs:

- Regional Infrastructure Fund (RIF)
- Regional Jobs Fund (RJF)
- Stronger Regional Communities Plan (SRCP)

Rural Development Program Stream

Investing in local infrastructure, creating opportunities for economic growth, and enhancing the appeal and liveability of rural towns and surrounding areas.



Productive and Liveable Cities & Centres Program Stream

Supporting significant infrastructure projects in regional cities, centres, and towns.

Enabling Infrastructure Program Stream

Supporting regional industries to innovate, build resilience, and improve their adaptability to changing economic and environmental conditions.

Community Capacity Building Program Stream

Developing and strengthening local people's capacity to make a difference in their communities.

Regional Skills Fund

A targeted, place-based regional skills grants program driven by industry in partnership with the tertiary sector, working to build local capacity, resilience, and support jobs creation.

Population Attraction Program Stream

Attracting groups, such as professionals and skilled labour, businesses, families, and young people to regional Victoria.

Community Road Safety Grants

The TAC offers community groups in Victoria the opportunity to apply for funding for road safety projects under the Community Road Safety Grants Program. This program aims to:

- Encourage community involvement in local road safety programs that are consistent with Victoria's Road Safety Strategy.
- Provide opportunities for local community groups to develop and implement effective road safety projects targeting specific local road safety issues.

Local Government Grants for Small-Scale Infrastructure

Local Government Areas (LGAs) in Victoria have the opportunity to apply for funding for small-scale infrastructure treatments to address pedestrian and cyclist safety under the Local Government Grants Program. This program aims to:

- Encourage Local Government involvement in cyclist and pedestrian safety projects that are consistent with the Towards Zero 2016-2020 Road Safety Strategy and Action Plan.
- Provide opportunities for LGAs to develop and implement low cost, effective infrastructure treatments targeting cyclist and pedestrian safety issues.

Principal Pedestrian Networks

Walking is the most participated in the form of active transport. In recognition of this, the department has developed guidelines to assist local councils to develop Principal Pedestrian Networks (PPNs).

The PPN process involves mapping out and planning for a higher quality walking environment on key routes to local activity centres such as shops, schools, and transport hubs.

4.6 Maps 2010-2017

In the 2010 Strategy, each proposed project together with the existing walking, shared paths, and cycle routes in each town was mapped by hand. It was intended that these maps would be made available to communities upon request to assist in their planning. It was also intended that the maps would be transferred to the SGSC Geographic Information System (GIS).

It is not in this review's scope to update the paths and trails maps again by hand, nor is it necessary as the bulk of the 2010 map information, i.e. the Shire footpath network has already been mapped on the GIS. The remaining completed shared paths, rail trails, walking tracks, and cycle lanes/routes still need to be mapped in the GIS and would be relatively achievable due to the small number completed.

The proposed paths and trails could also be mapped in their own 'layers' making all the proposals readily visible and available on demand.

Council will need to allocate extra resources for the completion of this mapping project.



4.7 2010 Project Priority Matrix (PPM)

The proposals identified in 2010 were prioritised based on the adoption and modification of '*Prioritisation of Bicycle Infrastructure Proposals*' commissioned by the Australian Cycling Council and prepared by Ian Ker and Adam Sidebottom, *ARRB Group Ltd Project No. WC5227 - December 2005*.

The weighting values were subjective and based on community and SGSC officer's observations, records, complaints database, accident counts, and personal experience. The PPM (and underlying spread sheet) was a live document and allowed for future modification or reprioritisation if other data become available, or when priorities changed.

It should be noted that prioritisation of bicycle infrastructure proposals require:

- Comparable information across a diverse range of initiatives.
- A framework for undertaking comparative assessment of that information.
- Techniques for handling information of various types and quality of information including:
 - Monetary
 - Quantitative, non-monetary
 - Qualitative
 - Descriptive
 - Analytically-derived
 - Politically derived
 - Policy-derived
 - Professional judgement

Traditionally, transport and related initiatives have been evaluated within a benefit-cost framework that is heavily reliant upon the quantification of outcomes and their conversion into monetary values. Whilst benefit-cost analysis is still a valid and necessary component of evaluation, it is insufficient to accommodate the broad range of government and community objectives that initiatives must increasingly address – often reflected in the shorthand of *triple-bottom-line* or

sustainability assessment. In this broader context, not all criteria will be measurable in quantitative terms. Emerging guidance on project appraisal, including national methodology being developed under the *AusLink* National Land Transport Plan, acknowledges the need for and value of both quantitative and qualitative measures in response to the broad range of criteria identified as being relevant. Current Australian practice in the area of infrastructure project evaluation ranges from formal multi-criteria analyses to subjective internal rankings.

A key priority for walking/cycling infrastructure was the completion of the strategic networks. Feedback received from stakeholders generally supported an outcome which produced prioritisation parameters that were⁵:

- Safe and easy to use;
- Developed specifically for walking/cycling rather than an adaptation of a road-based tool;
- Provided a clear ranked list of projects; and
- Enabled easy and robust justification of prioritised projects.

The PPM is designed as a decision-support system, rather than a prescriptive ranking toolkit. Recent developments in project prioritisation in transport have generally adopted a similar approach, but in the case of walking / bicycle facilities, less detailed than that proposed here.

The PPM is at the core of the proposed methodology and is structured in such a way that it reflects the prioritisation parameters identified by stakeholders. The PPM will not, in isolation, provide decision makers with a definitive list of projects using their associated scores or rankings. Instead, this approach presents the decision maker with all necessary information with which to make decisions.


To clarify, the importance of the PPM is in the consistent, comparable information for each proposal it presents by addressing fixed criteria and objectives. These features can be summarised as:

- Consistent and comprehensive information across all project proposals.

⁵ This feedback is derived from '*Prioritisation of Bicycle Infrastructure Proposals*' commissioned by the Australian Cycling Council and is used to reflect common outcomes of 'active transport' surveys.

- Quantitative and qualitative aspects for all criteria where applicable.
- Leaves the decisions in the hands of the decision makers.
- Values, objectives, and criteria could be based on stakeholder input/feedback (this needs to be developed).
- Facilitates the consideration of projects that are difficult to assess by traditional benefit cost analysis.
- Allows informed quantitative analysis using a simple multi-criteria analysis.

PPM Methodology Diagram

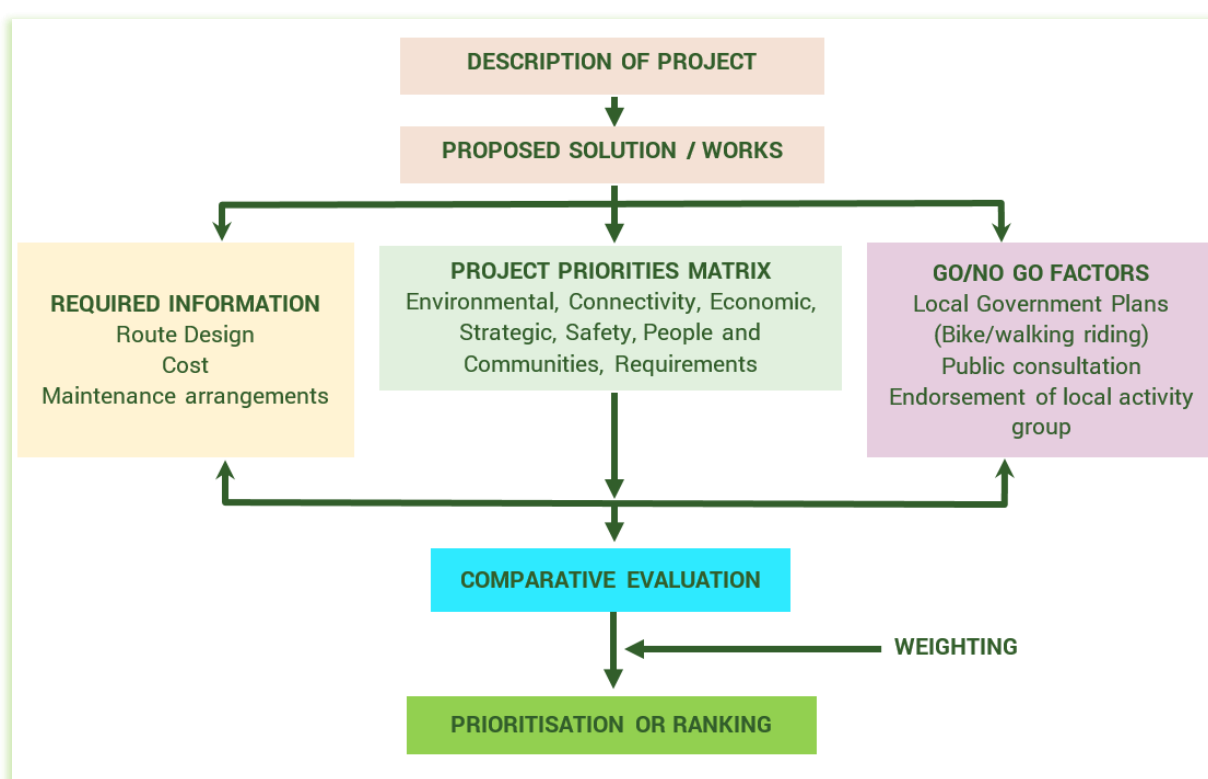

This methodology is a decision-support system which has the following aims to:

- Locate the responsibility of decision making with *decision makers*, not the proponents, analysts, or toolkit developers.
- Present all relevant information, both quantitative and qualitative, that will aid in the *decision-making process*.
- Allow easy comparison of proposals for the purposes of prioritisation.

The PPM is divided into seven (7) objectives and twenty (20) sub-objectives. Each sub-objective requires a qualitative impact assessment as well as the provision of appropriate measurements or estimates ('metrics') related to the criterion. In all

cases, a qualitative assessment is required. For the measurements or estimates related to the project, the proponent is asked to add whatever information or data they think is relevant to the proposal.

Given the disparate nature of proposals, directly comparable quantitative requirements are not possible when dealing with multiple projects. If a PPM was being used to assess a number of different options for the same problem (for example, a shared path versus a bridge at grade) then directly comparable quantitative measures should be prescribed in the assessment framework. This PPM recommends some indicative values which may be generic and relevant to a high proportion of projects but are by no means universal or comprehensive. For example, walking paths will have a universal '0' for the cycle values.

4.8 2018 PPM Revised

This review has recognised several issues surrounding the original 2010 PPM spreadsheet:

- It was large with 96 projects.
- Only identified project responsibility in a general fashion, not department / officer level.
- Included the Footpath Extension Program that was already operating independently with its own budget.
- Although considered complex, this helped spread the valuing process and reduce the subjectivity of the valuation process.
- Several significant omissions in the objectives e.g. environmental impacts, level of service / DDA compliance and catchment size, have been included in the revised 2018 PPM.

Projects of similar type can be readily sorted (using excel spreadsheet format) within the PPM and therefore readily compared when considered for funding.=

5. community consultation



5.1 Consultation Methodology

This desktop review / update of the 2010 Strategy has considered priorities highlighted from a broad range of inputs including community plans, town infrastructure blueprints, town infrastructure plans, community requests, meeting feedback notes, SGSC officer works programs, outcomes from the *Our Say* internet community consultation, budget submissions, section 223 submissions, and the Capital Works Program funding process amongst others.

5.1.1 Inputs into the 2017 Review of the 2010 Strategy



Inputs into the 2017 Review of the 2010 Strategy

Telephone discussions regarding individual proposals were held with lead community members and groups to help this review clarify their aims, gather extra data, and to confirm intentions on specific projects. Those spoken to include the Walkerville Residents and Ratepayers Association, Sandy Point Community Group, Prom Country Tourism, Friends of Agnes Falls, Mossvale Advisory Committee, and various unsuspecting shop keepers.

If the information available was sufficient to determine route, land ownership, user type, and estimate costs, the proponents weren't generally contacted. For example, the Hoddle Mountain Trail Management Group recently made a comprehensive



PowerPoint presentation to Council. This information together with that sourced from Council's internal data systems, including letters of opposition, were used in the ranking and analysis of that project.

During the individual discussions, the subject of the GSRT was briefly raised. The general consensus of those asked believed the GSRT and its future extensions could only contribute in the long term to the well-being of the broader community, eventually providing links and context to their specific projects.

On conclusion of the desktop review / update of the 2010 Strategy, a draft 2017 Strategy was placed on public exhibition for comment after the open briefing to Council and members of the public on 20 September 2017.

5.1.2 Future Community Consultation Methods

The internet is already being used by the SGSC in their community consultation process in the form of the *Our Say* feedback forum. This could be expanded to include an on-line project mapping forum. Several councils, such as Greater Dandenong City and Bass Coast Shire Council have used the internet to allow their communities to directly identify paths and trail opportunities in their municipalities.

This strategy employs innovative techniques to ensure the community enjoyed multiple opportunities to contribute. 'Crowd Spot', a visual consultation tool, enabled people to have their say online by sharing comments about specific geographic locations on an interactive map. Community members had the opportunity to identify spots where they liked or disliked to ride/walk and spots where they had an idea about how the location could be improved. This engagement tool was supported by community consultation, including paper based surveys and community conversations at designated events. At Greater Dandenong City, over 500 residents were engaged in the consultation phase, with 336 community members utilising the Crowd Spot Map. The results of the consultation informed the development of their Path & Trails Strategy and action plan.

*Example of the 'Crowd Spot' consultation process
Greater Dandenong City*



6. description & assessment of new projects



Several new off-road paths have been included in the 2018 Project List. Some have been driven by respective communities appreciating the benefits off-road paths and trails can bring to their local environment and several have been included because of their potential to provide Shire wide benefit.

Those that require significant further development are briefly described on the following page.

6.1 Great Southern Rail Trail (GSRT)

6.1.1 The GSRT: Leongatha to Nyora Extension

Due to the cessation of the Nyora to Leongatha tourist rail, an opportunity now exists to extend the GSRT from Leongatha through to Nyora via Ruby, Kardella, Korumburra, Bena, and Loch at a length of 43kms.

GSRT Extension - Leongatha to Nyora and Beyond



If the GSRT is extended to Nyora, it will become the second longest continuous rail trail in Victoria and be of national significance in terms of accessible rail trails.

This opportunity allows the development of the trail beyond the Shire boundary, linking it to the rail head at Cranbourne (or Clyde, if the suburban rail is extended).

As to when and how the GSRT extension to Nyora proceeds is dependent on external funding. Staging its development may be critical to its future success.

Options may include:

- A. Construct the GSRT the full length – Leongatha to the Shire boundary.

- B. Leongatha to Korumburra 14km – this allows the linking of the Shire’s two major population centres together with old station sites of Ruby and Kardella.
- C. Korumburra to Nyora including Bena and Loch.
- D. Develop the rail land and buildings in Leongatha and Korumburra, an option that allows significant community benefit in the short term for less capital outlay (for the trail). The inter town connections can be developed later.

Further to the above extensions, the rail reserve from Nyora to Anderson in the Bass Coast Shire provides further connectivity options. This option may be considered after all the above GSRT options have been completed rather than diverting users away to the Bass Coast Shire and the coast beyond via Anderson. After reviewing the Cardinia Shire’s Paths & Trails Strategy, it could be supposed that they have a similar strategy. Their strategy doesn’t propose extending the rail trail connections south to the South Gippsland Shire or north to the City of Casey. Instead they have focused their future trail developments a few kilometres either side of the townships Koo Wee Rup and Lang Lang. This approach may make linking Nyora with the suburban rail head difficult in the future.

GSRT - The Whole Picture Completed




As the Nyora-Leongatha tourist train operated up until a few years ago, most of the infrastructure should be sound enough to use for the rail trail. Some preliminary structural investigations confirm this. The extension of the trail from Welshpool to Hedley and beyond has not been used by trains for many years. Further feasibility and engineering reports would be required before costs can be apportioned.

Major rail trail road crossing designs, for example at the South Gippsland Highway in Leongatha, have not been resolved and may add substantially to the final cost of this Leongatha to Nyora section. This crossing design may be integrated with the Leongatha Station and Bair Street link development plans. Preliminary cost estimates are approximately \$1.5 million.

6.1.2 The GSRT: Welshpool to Hedley Extension

There is also an opportunity to extend the GSRT east from Welshpool to Hedley and beyond to Alberton, linking with the Wellington Shire's plans to take the 'Tara Trail' from Yarram to Port Albert, thereby creating a truly iconic piece of infrastructure, Cranbourne to Port Albert or Yarram.

GSRT Extension - Welshpool to Alberton (Yarram)

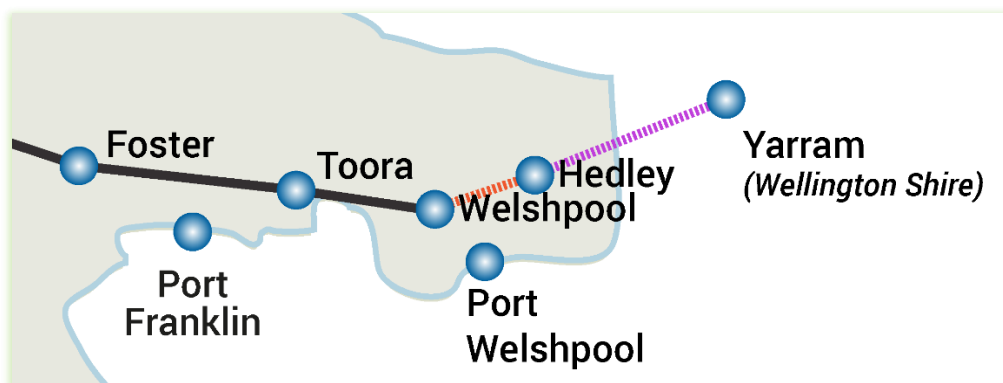

6.1.3 Future GSRT Management

Currently, the GSRT from Leongatha to Welshpool is on crown land and was managed by the GSRT CoM on behalf of DELWP. Due to increased complexity and the level of GSRT management required, the volunteer committee was finding it difficult to continue. Lack of volunteers has resulted in the committee's demise with the committee handing the responsibility back to DELWP in June 2017. DELWP have since appointed a new GSRT CoM.

To secure the proposed GSRT extensions, Council will need to consider a lease or license of the rail corridor and buildings from Vic Track. The total length will be over 120km.

The current budget available to the GSRT CoM for maintenance is approximately \$1,400 per kilometre for the 72 km length from Leongatha to Welshpool which totals around \$100,800 per annum. If Council were to ultimately take over responsibility for the full length of the trail, the recurrent maintenance costs are estimated to be around \$300,000 per annum⁶.

Friends groups located in each town could be allocated a section each to maintain. This could help to reduce the estimated maintenance cost, however, coordination and support by Council will need to be considered.

6.1.4 Consultation / Research

Consultation and research was restricted to:

- A desktop review of Council's relevant plans and strategies;
- Meeting with SGSC staff;
- Informal community discussions;
- Results from the 'Our Say' internet and site forums; and
- Results from adjoining Shires plans and strategies.

6.2 Hoddle Mountain Trail

The Hoddle Mountain Trail Management Group (HMTMG), a community based volunteer group, approached Council on 17 May 2017 with a proposal seeking Council support for the ongoing development of the 17-kilometre Hoddle Mountain Trail and recognition of the trail as a major community asset.

The proposal sought assistance from Council to upgrade its sections of the already used track to allow the HMTMG to maintain the trail into the future to an agreed standard.

⁶ Expansion of Great Southern Rail Trail and Lease of Station Buildings; Council Strategic Briefing Agenda - 15 March 2017

6.2.1 Consultation / Research


Consultation and research included:

- A desktop review off Council's relevant plans and strategies, letters, and submissions;
- Meetings with SGSC staff;
- Discussion with Prom Country Tourism representative; and
- Research into Council's mapping document and request handling systems for relevant information.

6.2.2 Hoddle Mountain Trail Route

The Hoddle Mountain Trail creates a loop intersecting with the GSRT at Fish Creek and to the north east at Mt Hoddle Road. The trail utilises Council road reserves, private land, internally skirts a quarry site, crosses South Gippsland Water land and links with the Loader Track providing spectacular views of Wilsons Promontory and Corner Inlet. Superficially, this appears to be a proposal that fulfils many of Council's and this strategy's aims. Refer to map on the following page.

Hoddle Mountain Trail Map

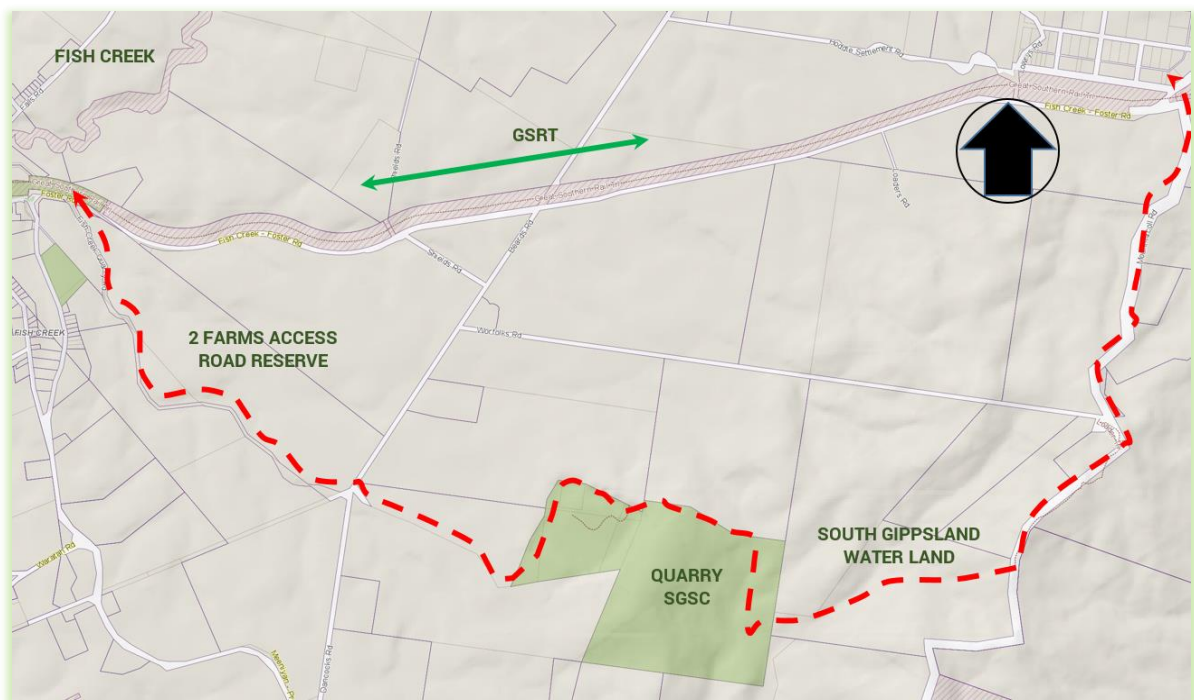

6.2.3 Mount Hoddle Trail Issues

Before any decisions regarding formal development and recognition of the trail can proceed, several issues need to be resolved regarding the current land tenure of the proposed route and the potential impacts the proposed route would have on the adjoining properties.

6.2.4 SGSC Resolutions

At the Ordinary Council Meeting on 26 April 2018, Council resolved that part of the Fish Creek Quarry Road, Fish Creek be opened for public traffic, as it has never been formally closed, and has a history of being continually traversed as a trail. Council are to commit \$4,000 to work on the trail as well as weed spraying maintenance, slashing, and installation of a pedestrian counter with usage of the trail reviewed after two years.

In regards to future management, at the same meeting, Council resolved to develop a memorandum of understanding with the HMTMG to establish management arrangements. A resolution was also made that the trail be maintained as a Grade Three Walking Trail in accordance with the Australian Walking Track Grading System.

At the Ordinary Council Meeting on 28 March 2018, Council resolved to transfer ownership of approximately 27 Ha of the existing quarry site (east of the quarry) to South Gippsland Water to preserve indigenous vegetation. This area encompasses part of the Hoddle Mountain Trail, therefore removing it from the boundaries of the quarry and resolving any conflict issues.

Hoddle Look-out



6.3 Waratah Way

The Sandy Point community, represented by the Sandy Point Community Group, has demonstrated a continued interest in the development of a shared path linking Sandy Point and Waratah Bay. Significant support has been shown by the local community and visitors through petitions, presentations etc., and the project has been listed in the Sandy Point Community Plan.

Two possible alignments for a shared path were identified by SGSC officers:

- **Option 1** follows the alignment of a previously cleared slashed fire break / weed management access, which is located at the base of the northern side of the sand dunes. This alignment is partly on crown land and partly on privately owned land.
- **Option 2** is entirely within crown land, however extends into the sand dunes by up to 45 metres and will require extensive vegetation removal and earthworks.

A consultant, Ethos NRM, was engaged to undertake a preliminary study of potential impacts and risks associated with these two possible alignments for a shared path from Sandy Point to The Gap carpark at Waratah Bay.

From the Ethos report, personal observation and document review (particularly historical evidence) **Option 2** must be considered un-feasible due to the potential damage the construction and the resulting user impact could have on a single crown dune system. This fragile system is all that separates valuable farm land from Waratah Bay.

For **Option 1** to become viable, the private land tenure issues need to be resolved (one way or another).

Some options may include:

- A. Purchase the private land. This could include a strip of cleared land, 5m north of the existing fence line providing some advantages:
 - Using cleared pasture would allow for ease of construction and reduce costs and time.

- Significantly reduce the need for further environmental studies, vegetation offsets (these will be very difficult to secure).

Note: if the point above is being considered, the path would have to still bend south into the dune system to avoid the shed complex and adversely affecting farm operations.

- This consideration still allows farm access for both foreshore and farm management purposes.
- B. Lease or rent the land on a long-term arrangement. Secure similar land area as suggested in the above point.
- It is generally felt that this proposal does not justify a compulsory acquisition process.
 - SGSC will need to lead this negotiation process as several adjoining landowners are strongly opposed to the proposal if this shared path is to proceed.

6.3.1 The Gap to Waratah Bay

Given that the purpose of the shared path was to link the two townships, a significant omission in the drive to develop the Waratah Way has been the resolution of *“where do the pedestrians, cyclists, and horse riders go after reaching The Gap from Sandy Point?”*

Apart from the beach, the current link could be along an existing path in the Waratah Bay foreshore (SGSC) to west of Waratah Camp and entering Gale Street, a 100kph speed limit road.

This road is flanked by hedged Banksia Woodland vegetation on the south foreshore side and very narrow shoulders both sides of the road seal. The northern side of the road reserve is cleared, with scattered mature Banksias and Melaleuca Thickets further west.

The road cuts through a large dune to the west creating steep embankments.

The powerline servicing Waratah Bay also runs through the northern strip of the road reserve. Immediately off the narrow shoulder on the northern side, the profile drops away into low lying land subject to inundation.

There are no easy solutions here.

One primary aim of the shared path is to provide a safe walking and cycling environment for users (or it won't be used, especially by families).

By designating the road as 'a shared path', Council has a duty of care to the users by applying recognised standards to achieve a safe passage.

Design standards (Austroads) require a minimum of 9 metres separation between walkers/cyclists etc. and vehicular traffic on a 100kph signed road or use of a physical separation barrier.

The 9 metre separation would be unachievable in the existing road reserve and a barrier ("W" section) would be prohibitively expensive (\$200 / lineal metre x 1,600 metres x 2 (both sides) = **\$600,000**).

Gale Street Looking West



Gale Street Looking West Dune Cutting / Power Pole





Solutions may include:

- Reduce speed limit to 80kph.
- Where possible (northern side) construct a 2.5 metre wide coloured sealed shared path delineated with flexible guide posts; the colour difference and posts act as visual triggers for the motorists.
- Would require substantial fill / earthworks.
- Land purchase of adjoining farmland, estimated area 625 metres x 5 metres, parallel to the fence line from Camp Waratah to the west of the dune cutting to avoid the dune and mature banksias.
- Purchase 1,666 metres x 5 metres of farm land parallel to the north side of Gale Street and completely avoid the road reserve. This still would require substantial earthworks due to the land being very wet. Avoids traffic, powerlines, dunes, and vegetation removal.

The preferred option would be the latter; a 2.5 metre wide compacted gravel shared path, with land purchase (by negotiation).

Cost estimated at **\$335,000**. This figure is subject to variation depending on the outcomes of further investigations and surveys.

Note: See *Appendix 3* for indicative costs for various options for The Gap to Waratah Bay (Gale Street) shared path.

Total Waratah Way cost:

- | | |
|--------------------------------|--|
| ■ Option 1 (Ethos 2016) | = \$525,000 |
| ■ Gale St land purchase option | = \$335,000 |
| Total estimated cost | = \$860,000 (conditional on the outcomes of surveys, Cultural Heritage Management Plan (CHMP), vegetation offset requirements, land purchases). |

6.3.2 Consultation / Research

Consultation and research included:

- A desktop review of Council's relevant plans and strategies including the Ethos report and others.
- Review of community plans, letters, and submissions.
- Meetings with SGSC staff.
- Informal community discussions with the project's proponents.

6.3.3 Map of Waratah Way



Possible path route scenario using farm land:



6.3.4 Outcomes of Community Consultation

A community consultation meeting was held at the Sandy Point Community Hall on 3 May 2018 with members from the Sandy Point Community Group, the Sandy Point Foreshore Committee, two Councilors, SGSC Officers, and a representative from Ethos NRM (environmental consultant).

Ethos NRM presented their Preliminary Geomorphological and Ecological Investigation report on the environmental issues related to the location of a shared path between Sandy Point and Waratah Bay.

There were several items raised at the meeting by the Sandy Point Community Group including:

- The project not being listed on the Project List.
- The lack of community consultation to this point.
- The reluctance by Council to compulsorily acquire private farm land to accommodate the path.
- A lack of acknowledgement of the benefits of the path.

SGSC officers acknowledge the benefits of the trail to the community and visitors, and that a shared path accommodating walkers, cyclists, and horse riders would be a great asset for the area.

After assessing the two proposed path alignment options, it is felt that the environmental impacts of **Option 2**, located on crown land through the single crown dune system, makes this option unviable.

Path alignment in **Option 1** through the privately owned farm land requires acquisition of land.

The path was not going to be placed on the 2018 Project List (**Appendix 1**), however the below Council resolution requires it to be reinstated, with **Option 1** being considered by Council in the future when the Sandy Point Community Group and Foreshore Committee resolve the land tenure issue with the owners of the adjacent farm land.

COUNCIL DECISION

At its Ordinary Meeting 30 May 2018, Council considered the report on the draft 2018 Paths and Trails Strategy and resolved the following with respect to the Waratah Way trail:

THAT COUNCIL:

1. **HAVING CONSIDERED ALL SUBMISSIONS RECEIVED FROM THE PUBLIC, ADOPTS THE 2018 PATHS & TRAILS STRATEGY (ATTACHMENT [3.2.1]), INCLUDING:**
 - a. **THE 'WARATAH WAY' PATH/ TRAIL IN THE PROJECT LIST:**
 - i. **THAT THE WARATAH WAY PATH IS UNFUNDED AND NEEDS FURTHER INVESTIGATION BY THE COMMUNITY, AND**
 - ii. **THAT THERE WILL BE NO COMPULSORY ACQUISITION OF FARM LAND FOR THE PROJECT, TO GIVE SURETY TO PROPERTY OWNERS.**

6.4 Acacia Way, Walkerville

The Walkerville Residents and Ratepayers Association Inc. are proposing the construction of an 800-900 metre long pedestrian safety walking path along Acacia Road (Fish Creek - Walkerville Road) Walkerville. The purpose is to allow residents and visitors to the Promontory Views Estate to safely walk from the estate along Acacia Street allowing access to the existing tracks that lead to lookouts over Waratah Bay to Wilsons Promontory and further south to the path system in the Cape Liptrap Coastal Park. One track leads down the escarpment onto the beach at the rear of the Walkerville Caravan Park.

The route would run parallel to Acacia Road on the eastern side either:

- In the road reserve skirting the power poles; or
- Immediately adjacent to the road reserve in the Cape Liptrap Coastal Park. This is crown land managed by Parks Victoria.

The image below is from the Walkerville Residents and Ratepayers Association grant submission to SGSC in 2016.

Site Plan – Proposed Waking Path



TO THE FORESHORE

This proposal consists of a 900 metre, 2.5 metre wide compacted gravel shared path with 4 x 4 metre long timber boardwalks at an estimated cost of **\$92,000**.

Issues include:

- Siting of path, i.e. road reserve or crown Land adjacent.
- Future maintenance responsibility.
- How will powerline maintenance vehicles, Parks Vic, and CFA vehicles etc. effect/impact the gravel path when they need to access the coastal park?
- What happens to users at the southern end near the Walkerville / Cape Liptrap intersection? Ideally, they cross Acacia Road to access the walking paths to the beach.

6.4.1 Consultation / Research

Consultation and research included:

- A desktop review of SGSCs relevant plans and strategies and others.
- Review of community plans, letters, and submissions.

- Meetings with SGSC staff.
- Informal community discussions with the project's proponents.

6.5 Walkerville Foreshore Shared Path

Together with the upgrade of the seawall and parking area at Walkerville North, the Walkerville Foreshore Reserve Committee of Management has proposed the construction of a 1,335 metre (approx.) shared path along Bayside Drive, from the caravan park in the north to the boat ramp in the south. This proposal will be addressed in more detail in the forthcoming Walkerville Foreshore Management Plan.

Briefly, it will allow the safer passage of walkers and cyclists along the foreshore (beachside). Currently users meander along either side of the road verge.

Issues to consider:

- The width of the existing shoulder.
- The extent of coastal erosion.
- Vegetation removal required.
- Bridges and boardwalks over creeks and drains.
- Powerlines are in the eastern side of the road reserve.

6.6 Mossvale Park

The Mossvale Park Committee of Management (a section 86 committee to Council) intends to include in their 2018 Mossvale Park Management Plan, an extended network of paths within the park to allow all ability access to views currently inaccessible to many visitors.

The original 1998 Management Plan by Andrew Paget included boardwalks across the wetter flood prone areas and graded gravel paths connecting existing paths and points of interest to the hill overlooking the park. The current proposal builds on that initial 1998 concept and will allow all users in most weather conditions access to the superb tree plantings and views found on the hill. The current popularity of the park (particularly during concerts and events) has been adding pressure to the

park's environment by introducing large numbers of people to the park. Without the corresponding infrastructure that would help manage and minimise the negative impact to the many heritage listed trees, compaction and vandalism will continue to pose a threat. The path network will create a circuit and add interest by appropriately guiding visitors around the park between points of interest thereby adding value to an already iconic park.

Details will be developed in the proposed 2018 Mossvale Park Management Plan.

6.6.1 Consultation / Research

Consultation and research included:

- A desktop review off SGSCs relevant plans and strategies and others.
- Review of community plans, letters, and submissions.
- Meetings with SGSC staff.
- Informal discussions with the project's proponents.
- On site visit.

6.7 Agnes River Road Walk

This walk leads from the GSRT north along Gassons Road, across the South Gippsland Highway, then north along the Agnes River Road via made and unmade road reserves to the Agnes Falls Reserve. The proposal consists of a gravel shared path approximately 5 km long. This track traverses some very steep hill country allowing for extensive views of Corner Inlet and Wilsons Promontory. Historically a through-road until the death of a grader operator in the 1960s, the route has continued to be used by walkers and horse riders and may be open in the future to adventurous cyclists. This proposal is in its very early stages of development (SGSC did a desktop cost estimate) and has been included in the review to acknowledge its potential.

View from Agnes Falls Road South to Wilsons Promontory



6.7.1 Consultation / Research

Consultation and research included:

- A desktop review of SGSCs relevant plans and strategies and others.
- Review of community plans, letters, and submissions.
- Meetings with SGSC staff.
- Informal discussions with the project's proponents.



6.8 Mountain Bikes

Mountain Bike circuits are growing across Australia as the sport develops. Being an Olympic sport has given the sport some high-level credibility throughout the riding fraternity. The development of circuits such as the one at Forrest in the Otway Ranges has given the township a much-needed boost (www.rideforrest.com.au). A new brewery and shops sees the town full of riders and visitors on most weekends. This circuit hosts local, state, and national competitions and is open to all users during the week.

As many more of these mountain bike circuits are springing up, it would seem South Gippsland, with its natural attractions, is missing out on this opportunity. Nothing has progressed in seven years after the 2010 Strategy identified mountain bike riding as a new tourism venture catering for a younger demographic.

Recently, a meeting was held in Foster resulting in the formation of a Mountain Bike Club. The Gippsland Mountain Trail Bike group (MTB) assisted in the development of this embryonic club by guiding members through the process. The Gippsland MTB Inc. is an active mountain bike association established to support and encourage the sport of mountain biking in Gippsland.

A mountain bike trail runs through Cement Creek Natural Features Reserve (Parks Vic) linking to the GSRT at Foster Station Park. The circuit of 5km was used for a mountain bike championship held in February 2015. This site presents SGSC with a great opportunity to support this fledgling group and thereby opening the sport to the wider community with an Olympic standard course. The Prom Coast MTB has plans to develop the Cement Creek Natural Features Reserve into a world class mountain bike facility.

Several other sites in South Gippsland hold informal club events and are used in an ad hoc manner. The sites are Mirboo North (plantation private land), Hallston (also has motorbike conflict issues), and Wuchatsch Reserve (SGSC) north of Nyora. None of these sites are formalised MTB trails and there can be regular conflict issues between land managers and differing users.

Ideally these four sites could be developed to cater for a range of users, each site offering different challenges e.g. cross country (an Olympic event), cyclo cross, downhill, gravity enduro, marathon, trials, school events, and 24-hour events to name a few.

6.9 Coal Creek to Ritchies Reserve

It is recommended that this “missing link” in the walking trail be included in the strategy to facilitate completeness of this trail. Subject to further investigation, it maybe be possible to complete the trail using a footpath extension, in which case it would be included in the Footpath Extension Program.

6.10 Isabella Blvd to Hannah Rise Crescent Shared Path


This is recognised and shall be a requirement of future sub-divisions in the area between Isabella Boulevard and Hannah Rise Crescent.

7. 2018 strategy review



It is proposed to conduct an annual desktop review / update of the 2018 Strategy on a 10 year cycle.

8. 2018 action plan

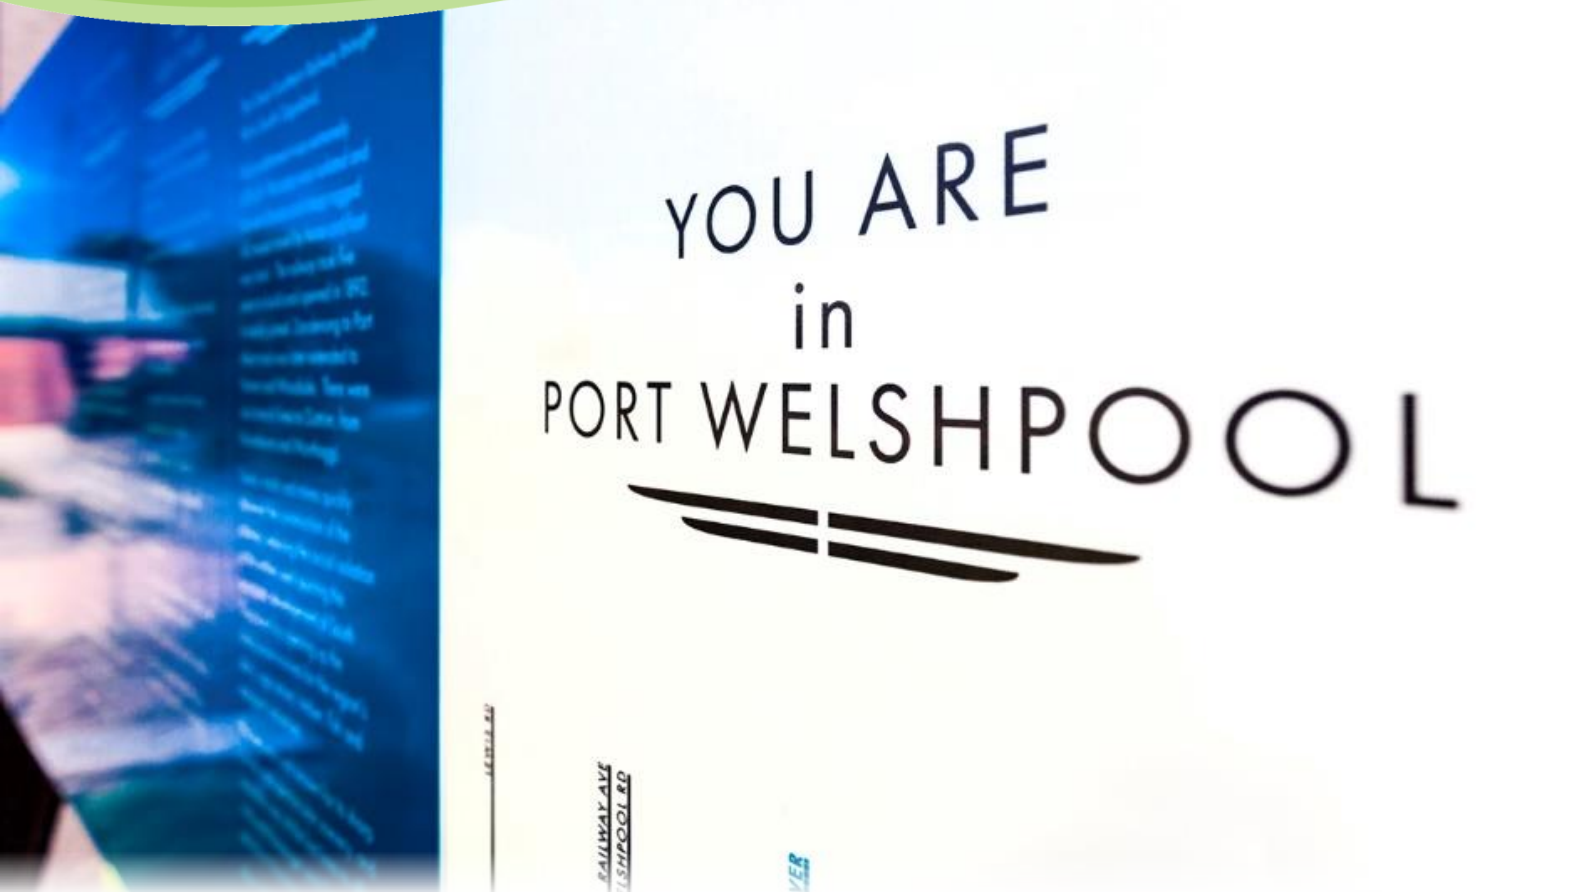

The following table sets out the 2018 Paths & Trails Strategy Action Plan that includes Marketing, Education, Management, and Development with the aim of making South Gippsland environments conducive to cycling, walking, and horse riding, maximising economic opportunities and increasing the residents' quality of life. The actions are for consideration by the relevant organisations. As most are unfunded, they will need consideration in future budgets.

8.1 2018 Strategy Action Plan

	STRATEGY / ACTIONS	LEAD ORGANISATION	TIME FRAME
1	Promotion & Encouragement		
1.1	The SGSC provide strong advocacy for the continued development of the GSRT.	SGSC, GSRT CoM DELWP Vic Track	SGSC Priority Project 2017/18
1.2	The SGSC actively source funding opportunities in conjunction with other government authorities to enable the development of the Korumburra and Leongatha (and others) station sites as community assets.	SGSC (Strategic Planning & Community Strengthening Units), Vic Track	2-4 years
1.3	Ensure that accommodation providers and tourist information centres provide up to date information regarding cycling / walking / riding opportunities in the region through the production (as required) of information brochures.	SGSC (Economic Development & Tourism Unit)	Ongoing
1.4	Continue to assist clubs and organisations to lobby for and stage major cycling/walking and equestrian events and tours to use the Region.	SGSC (Economic Development & Tourism, Community Strengthening Units)	Ongoing
1.5	Encourage the development of bicycle hire opportunities in Foster, Mirboo North, Korumburra and Leongatha.	SGSC (Strategic Planning, Economic Development & Tourism, and Community Strengthening Units)	Ongoing
1.6	Encourage accommodation providers to meet the needs of touring and recreational cyclists, (i.e. safe bicycle storage provision).	SGSC (Economic Development & Tourism Unit)	Ongoing

	STRATEGY / ACTIONS	LEAD ORGANISATION	TIME FRAME
1.7	Update Council's mapping system to reflect current paths and trails across the Shire.	Assets, GIS mapping	Ongoing
2	Marketing		
2.1	Increase the profile of South Gippsland as a walking, cycling and riding destination.	SGSC (Economic Development & Tourism Unit)	2-5 Years
3	Education & Encouragement		
3.1	Council could provide leadership for the development of special events and services to encourage a greater level of cycling, walking and riding amongst all members of its community.	SGSC (Community Strengthening Unit)	Ongoing
3.2	Continued assistance to and sponsorship, when funding / grants available, of organisations and programs that facilitate bicycle, walking, and riding education programs, particularly schools. Continue to support VicHealth's Walk to School program and associated activities.	SGSC (Social Planning Unit)	Ongoing
3.3	Get behind the promotion of local, regional, and state wide cycling encouragement events and programs, such as the 'Ride to Work Day'.	SGSC (Community Strengthening Unit)	Ongoing
4	Infrastructure		
4.1	Undertake maintenance of existing pedestrian / cycling assets including paths, trails, signs and information boards in accordance with a maintenance plan and budget of controlling / management organisations.	GSRT CoM, SGSC & other management organisations	Ongoing
4.2	In accordance with the priorities identified in Appendix 1 adopt and implement as funding becomes available. Include	SGSC	1-10 years



	STRATEGY / ACTIONS	LEAD ORGANISATION	TIME FRAME
	allowances in annual budgets for maintenance.		
4.3	Advocate for a Municipal Bicycle Network, a Regional Bicycle Network, and recreation links, for details see Appendix 1 in conjunction with maps.	SGSC Priority Project (All Units)	0-10 years
4.4	Advocate for responsible authorities to consider adopting a policy of sealing shoulders on roads where double centrelines occur for the safety of cyclists.	SGSC (Infrastructure Planning & Infrastructure Delivery Units)	Ongoing
4.5	Provision of permanent 'noticeboard' type maps as part of any cycling, pedestrian, riding facility development, particularly along 'shared paths', when funding becomes available.	SGSC, GSRT CoM	0-10 years
4.6	Review all projects requiring on-road line marking for compliance with bicycling design standards.	SGSC	1 year
5	Management & Development		
5.1	Council will consider, if changes are made to any road, the provision for cyclists will be assessed as part of the road design. Council will also closely liaise with VicRoads to consider, in any new designs for Highways or arterial road realignments, the provision of safe and convenient pedestrian crossings and bicycle facilities.	SGSC (Strategic Planning, Infrastructure Planning, and Infrastructure Delivery Units)	Ongoing
5.2	Formation of a coordination committee or similar to oversee the implementation of the South Gippsland region bicycle, walking, riding, paths, and trails facilities and that it be made up of one representative from each of the following organisations: <ul style="list-style-type: none"> ■ SGSC 	SGSC (Community Strengthening Unit)	0-1 year

	STRATEGY / ACTIONS	LEAD ORGANISATION	TIME FRAME
	<ul style="list-style-type: none"> ■ VicRoads ■ DELWP ■ Parks Victoria ■ Prom Country Tourism, and ■ adjoining shires 		
5.3	<p>Collect data to help support or clarify project priority assumptions (PPM). This data will in turn assist in Council's decision making process. Sophisticated counting techniques, (student driven) surveys of users, economic modelling, and surveys of businesses regarding cause and effect of decisions associated with the <i>Paths & Trails Strategy</i> be undertaken when resources / funding becomes available.</p>	SGSC (Economic Development & Tourism Unit)	Ongoing

9. appendices



9.1	2018 Project List	p.57
9.2	Costs Table	p.60
9.3	Gale Street Preliminary Costs for “Waratah Way”	p.63
9.4	References	p.65

appendix 1

9.1 2018 Project List

9.1.1 Construction Projects

Projects	Budget	Comments
Current Funded Projects		
Great Southern Rail Trail - Leongatha to Nyora	\$6M	Budget allocated in FY 19/20 & 22/23
Great Southern Rail Trail - Welshpool to Hedley (Shire boundary)	\$1M	Budget allocated in FY 18/19
Great Southern Rail Trail - Nyora to Shire boundary	Included in above budget	Part of the budget allocated in FY 22/23
Leongatha: Bair St laneway between no 21 and 23 Bair St to station	\$4.55M	Part of Bair St Streetscape Project. Budget allocated in FY 19/20.
Venus Bay: Van Cleef Reserve path network	\$110K	Developed in Master Plan (FY 17/18). Budget allocated in FY 18/19.
Future Unfunded Projects		
Great Southern Rail Trail - Nyora to Anderson	Nil	Further investigation required.
Leongatha: From MacDonald St reserve, along Coalition Creek reserve, Boags Rd to GSRT	Nil	Further investigation required.
Leongatha: Shared path from Louise Simon Crt to MacDonald St	Nil	Further investigation required.
Walkerville North: Bayside Drv, along beachside shoulder of road reserve	Nil	Further investigation required.
Nyora: Pony Club to Nyora Common along Patman Drv	Nil	Further investigation required.
Walkerville: Acacia St path	Nil	Further investigation required.
Loch: Loch Lap – Sunnyside Park along Hwy reserve and along western entrance to bus stop, then pick up / connect to existing footpath	Nil	Further investigation required.



9.1.1 Construction Projects

Projects	Budget	Comments
Waratah Way ⁷ : shared path linking Sandy Point and Waratah Bay	Nil	Further investigation by the community.
Toora: Agnes Falls link to the GSRT	Nil	Further investigation required.
Korumburra: Skip Walking Track. Creek reserve, existing road & rail reserves including Coal Creek to Ritchies Reserve link (almost complete)	Nil	Further investigation required.
Foster: Stockyard Creek, Pearl Park to GSRT	Nil	Further investigation required.
Berrys Creek: Internal path network at Mossvale Park	Nil	Further investigation required.
Coastal Walking Track: Venus Bay, Cape Liptrap, Bell Point, Walkerville, Waratah Bay, Sandy Point, Shallow Inlet, Adams Rd, Yanakie, Shellcott Rd, Port Franklin, Barry Beach, Port Welshpool. Incorporating Cooks Creek, Waratah Bay Walk, etc	Nil	This is primarily a walk along existing paths, beaches, cliff tops, and roads following the coast. It is not a new construction project but a project around way finding signage and directional walking maps.
Foster: Mountain Bike circuit	Nil	Council to advocate for this project
Mirboo North: Mountain Bike circuit	Nil	Council to advocate for this project
Nyora: Mountain Bike circuit, Wuchatsch Reserve	Nil	Council to advocate for this project
Hallston: Mountain Bike circuit	Nil	Council to advocate for this project
Korumburra: Shared path Isabella Blvd to Hannah Rise Crs	Nil	To be constructed as part of a future sub division.

⁷ **Waratah Way** – Ordinary Council Meeting 30 May 2018, Council resolved “that there will be no compulsory acquisition of farm land for the project, to give surety to property owners...”

9.1.2 Linemarking and Signage Projects

Projects	Budget	Comments
Future Unfunded Projects		
Foster: Station St, from Pearl Park linking to Rail Trail	Nil	Further investigation required.
Korumburra: Shellcot Rd, Guys Rd to Ayrle Park Crs	Nil	Further investigation required.
Sandy Point: Acacia St, Graeme Grv, Woodland Ave to Manuka St, link to Ray Henderson Walk	Nil	Further investigation required.
Korumburra: Victoria St, Bridge St to Recreation Reserve / Showground	Nil	Further investigation required.
Venus Bay: Canterbury Rd, linemarked cycle lanes, shops to Lees Rd, No. 3 Beach Rd to 3rd Estate & return	Nil	Further investigation required.
Leongatha: Young St, McCartin St to Bruce St then to Holt St	Nil	Further investigation required.
Korumburra: Princes St, Bridge St to Jumbunna Rd	Nil	Further investigation required.
Meeniyan: Hanley St, linemarking & signage	Nil	Further investigation required.
Korumburra: from George St to Victoria St	Nil	Further investigation required.
Korumburra: South Railway Crs from Walters Mine to Mionis St & Coal Creek	Nil	Further investigation required.
Venus Bay: Possible linemarked cycle lane Lees Rd, one way west to east	Nil	Further investigation required.
Venus Bay: Circuit from Fishermans Jetty to Canterbury Rd	Nil	Further investigation required.
Leongatha: Roughead St, South Gippsland Hwy to Yarragon Rd / Wild Dog Rd intersection	Nil	Further investigation required.
Tarwin Lower to Walkerville / Fish Creek	Nil	Further investigation required.
Korumburra: Bridge St, Princes St to Victoria St	Nil	Further investigation required.
Leongatha: Peart St, Allison St to McCartin St	Nil	Further investigation required.
Korumburra: Richard St, Princes St to South Railway Crs	Nil	Further investigation required.
Korumburra: Station St, Bridge St to Bourke St	Nil	Further investigation required.
Leongatha: Turner St - South Gippsland Hwy, east to Roughead St	Nil	Further investigation required.

9.1.3 Projects on VicRoads Roads

Projects	Budget	Comments
Current Funded Projects		
Korumburra: Jumbunna Rd, Secondary College to Guys Rd	\$922.5K	Budget allocated in FY 18/19.
Future Unfunded Projects		
Leongatha: South Gippsland Hwy, Allison St to McCartin St	Nil	Further investigation required. Council to advocate for this project
Leongatha: Ogilvy St, including South Gippsland Hwy intersection south-east to the Secondary College main entrance	Nil	Further investigation required. Council to advocate for this project
Leongatha: Bass Hwy/McCartin St, from cemetery to Peart St	Nil	Further investigation required. Council to advocate for this project
Korumburra: Radovick St, Guys Rd to Commercial St (South Gippsland Hwy)	Nil	Further investigation required. Council to advocate for this project
Leongatha: South Gippsland Hwy, the Bridge to Anderson St	Nil	Further investigation required. Council to advocate for this project
Foster to Wilson's Prom – Foster-Prom Rd	Nil	Further investigation required. Council to advocate for this project
Leongatha: to Inverloch Rd (Bass Hwy) cycle lanes	Nil	Further investigation required. Council to advocate for this project
Foster to Wilson's Prom, Fullers Rd, Black Swamp Rd, Foster-Prom Rd. Lester Rd, Shallow Inlet, Millar Rd, Foster-Prom Rd	Nil	Further investigation required. Council to advocate for this project
Meeniyah to Tarwin Lower – via Lower Tarwin Rd, linemarked cycle route, 2-way signed	Nil	Further investigation required. Council to advocate for this project
Nyora: Davis St/Forster Dr to Glover Rd, links develop zone	Nil	Further investigation required. Council to advocate for this project
Foster: Fish Creek Foster Rd, from Reserve St to Pioneer St / Bridge St, ie Swimming pool via Secondary College to Town centre	Nil	Further investigation required. Council to advocate for this project
Welshpool: South Gippsland Hwy (Main St) – cycle lanes Primary School to walk bridge. Investigate off-road facility	Nil	Further investigation required. Council to advocate for this project
Mirboo North: Strzelecki Hwy - Balook St to left turn prior to Grand Ridge Rd	Nil	Further investigation required. Council to advocate for this project
Leongatha to Mirboo North	Nil	Further investigation required. Council to advocate for this project

appendix 2

9.2 Costs Table

ITEM	UNIT	\$/UNIT
Line Marking 100m		
▪ continuous	lm	\$5.00/
▪ dotted	lm	\$1.00/
▪ bicycle stencil	each	\$80.0
▪ Line infill	m ²	\$40./m ²
Supply & install sign & post	each	\$250
4" X 2" pine edging	lm	\$15.00
Earthworks general	m ³	\$40
Concrete path, 2.5m wide	lm	\$200
Concrete path, 1.5m wide	lm	\$130
Gravel path, 2.5m wide	m ²	\$40
Asphalt path (hot mix), 2.5m wide	m ²	\$75/m
Tree clearing	lm	\$15
Road shoulder – bitumen	km	\$40-50,000
Road shoulder – gravel	km	\$20-25,000
Bituminous primer seal	m ²	9
Excavation for path - estimate	m ³	10
Supply, place, and compact gravel base	m ²	40
Bituminous primer seal (road verge pathway)	m ²	9
Concrete kerb	m	110



ITEM	UNIT	\$/UNIT
Supply & install 'W' section guardrail	lm	200
Culvert drain extension 1x225 dia. RRJ RCP	ea.	300
Culvert drain extension 1x300 dia. RRJ RCP	ea.	410
Culvert drain extension 1x450 dia. RRJ RCP	ea.	600
Culvert drain extension 1x525 dia. RRJ RCP	ea.	750
Culvert drain extension 1x900 dia. RRJ RCP	ea.	2100
Boardwalk (timber)	m ²	400
Supply and install bollards	ea.	100
Supply and install seats	ea.	2000
Supply and install picnic table and seating unit	ea.	2400
Supply and install bicycle rails	ea.	400
Relocate existing signage	ea.	60
Geofabric placed on unstable ground	m ²	2

appendix 3

9.3 Gale Street Preliminary Costs for “Waratah Way”

The following estimates are for a shared path from the ‘Waratah Camp’ exit to the Gale St reserve, Waratah Bay, assuming the existing path from ‘The Gap’ to opposite Waratah Camp is suitable. Length 1900 metres.

ITEM	UNIT	\$/UNIT	*REFER TO NOTES BELOW			
			OPTION A	OPTION B	OPTION C	OPTION D
Distance			1900	1900	1900	625
Land purchase price					4165	1562
Widen road shoulders (path width metres)			2.0	2.5		
Clear vegetation (some sections will not need clearing)	m ²	15	71250	17812.50		
Earthworks fill and form up low areas	m ³	40	-	76000	130000	
Path type						
Compacted gravel rolling surface as per GSRT (DeMerlos?) @150mm depth	m ²	15	114000	71250	201250	
Spray seal buff coloured (including forming & gravel base)	m ²	35	266000	166250	296250	
Asphalt seal buff coloured (including forming & gravel base)	m ²	60	399000	199500	415000	
Concrete (including forming & gravel base)	m ² @100mm	120	684000	342000	700000	
Guideposts	ea	40	28500	14250		
Signage x 4	ea	200	500	500		
Boardwalk	lm	400			1300000	



ITEM	*REFER TO NOTES BELOW			
	OPTION A	OPTION B	OPTION C	OPTION D
Totals				
Compacted gravel	214250	179812.50	335915	
Spray seal	366250	198812.50	300915	
Asphalt	499250	232062.50	419665	
Concrete	898250	450562.50	704665	
Additional costs include extension of studies quoted in Ethos report eg. Vegetation offsets, CHMP, drainage. Note: very wet low lying area, survey, design etc still required.				

OPTIONS

- A. Gale St @ 80km/h road reserve (r/r) both sides 2.0m wide off shoulder.
- B. North side r/r only @ 2.5 m wide away from shoulder in r/r may have to bend / narrow path to allow for power poles.
- C. Purchase farm land 5.0m wide easement for a 2.5m wide path.
- D. Purchase farm land 5.0m wide easement for a 2.5m w path from Waratah Camp then onto r/r.

appendix 4

9.4 References

9.4.1 Design Standards

- Austroads Guide to Road Design - Part 6A: Pedestrian and Cyclists
- Austroads Pedestrian-Cyclist Conflict Minimization on Shared Paths and Footpaths
- AP-G88-17 Cycling Aspects of Austroads Guides
- Universal Design Principles
- SGSC Infrastructure Design Manual
- Prioritisation of Bicycle Infrastructure Proposals; Australian Bicycle Council
- VicRoads; SmartRoads February 2015 Guidelines

9.4.2 Strategic Documents

National

- Gearing up for Active and Sustainable communities: Australian National Cycling Strategy 2011-16
- National Cycling Strategy 2011-16 2016 Implementation Report Austroads

State

- Summary_Cycling_Participation_Survey_2017_Vic
- Shared Paths Position Statement Victoria walks
- Victorian-Cycling-Action-Plan-2013-14 (1)

Local Plans and Strategies

- SGSC Council Plan 2017
- Asset Management Strategy 2017 (26 April 2017)
- Community Strengthening Strategy 2008 – 2010 (21 May 2008)

Review of the 2010 Paths & Trails Strategy



- Economic Development & Tourism Strategy 2015-2020
(26 November 2014)
- Long Term Financial Strategies
(14 December 2016)
- Paths & Trails Strategy 2010
(24 November 2010)
- Recreational Vehicle Strategy
(28 May 2014)
- Road Management Plan
(28 June 2017)
- Social Community Infrastructure Blueprint
(24 September 2014)
- Mirboo North Community Report
- Nyora Community Plan Final 2010
- Loch Community Plan Final 2010
- Mirboo North Structure Plan
- Leongatha Streetscape Master Plan
- Foster Community Report 2016
- Foster Community Infrastructure Plan 2016
- Leongatha Community Infrastructure Plan 2014
- Korumburra Structure Plan 2014
- Venus Bay Community Report
- Korumburra Engagement Plan
- Tarwin Lower Venus Bay Community Infrastructure Plan
(June 2014)
- Seasonal Population Impacts in Coastal Towns Plan 2015
- Waratah Bay Foreshore Management Plan 2015
- Nyora Development Strategy 2016
- Sandy Point Updated Community Plan
(May 2016 v.2)
- Cape Liptrap Coastal Park Management Plan, Parks Vic
- Walkerville Foreshore Management Plan
- Foster Streetscape Design

- Preliminary Geomorphological and Ecological Investigation:
Sandy Point to Waratah Bay Shared Path 2016, Ethos NRM Pty
Ltd
- Off Road Shared Trail between Sandy Point and Waratah Bay
Presentation to SGSC (17 May 2017)
- Hoddle Mountain Trail Management Committee
Presentation to SGSC (17 May 2017)
- Meeniyan Structure Plan
(July 2013)

SOUTH GIPPSLAND SHIRE COUNCIL

paths & trails strategy 2018



*A review and update of the 2010 Paths & Trails Strategy and policy
review that includes a prioritised and costed project list with descriptions.*



*South Gippsland
Shire Council*
